


Community Regeneration Partnership

March Cabinet
Programme Update



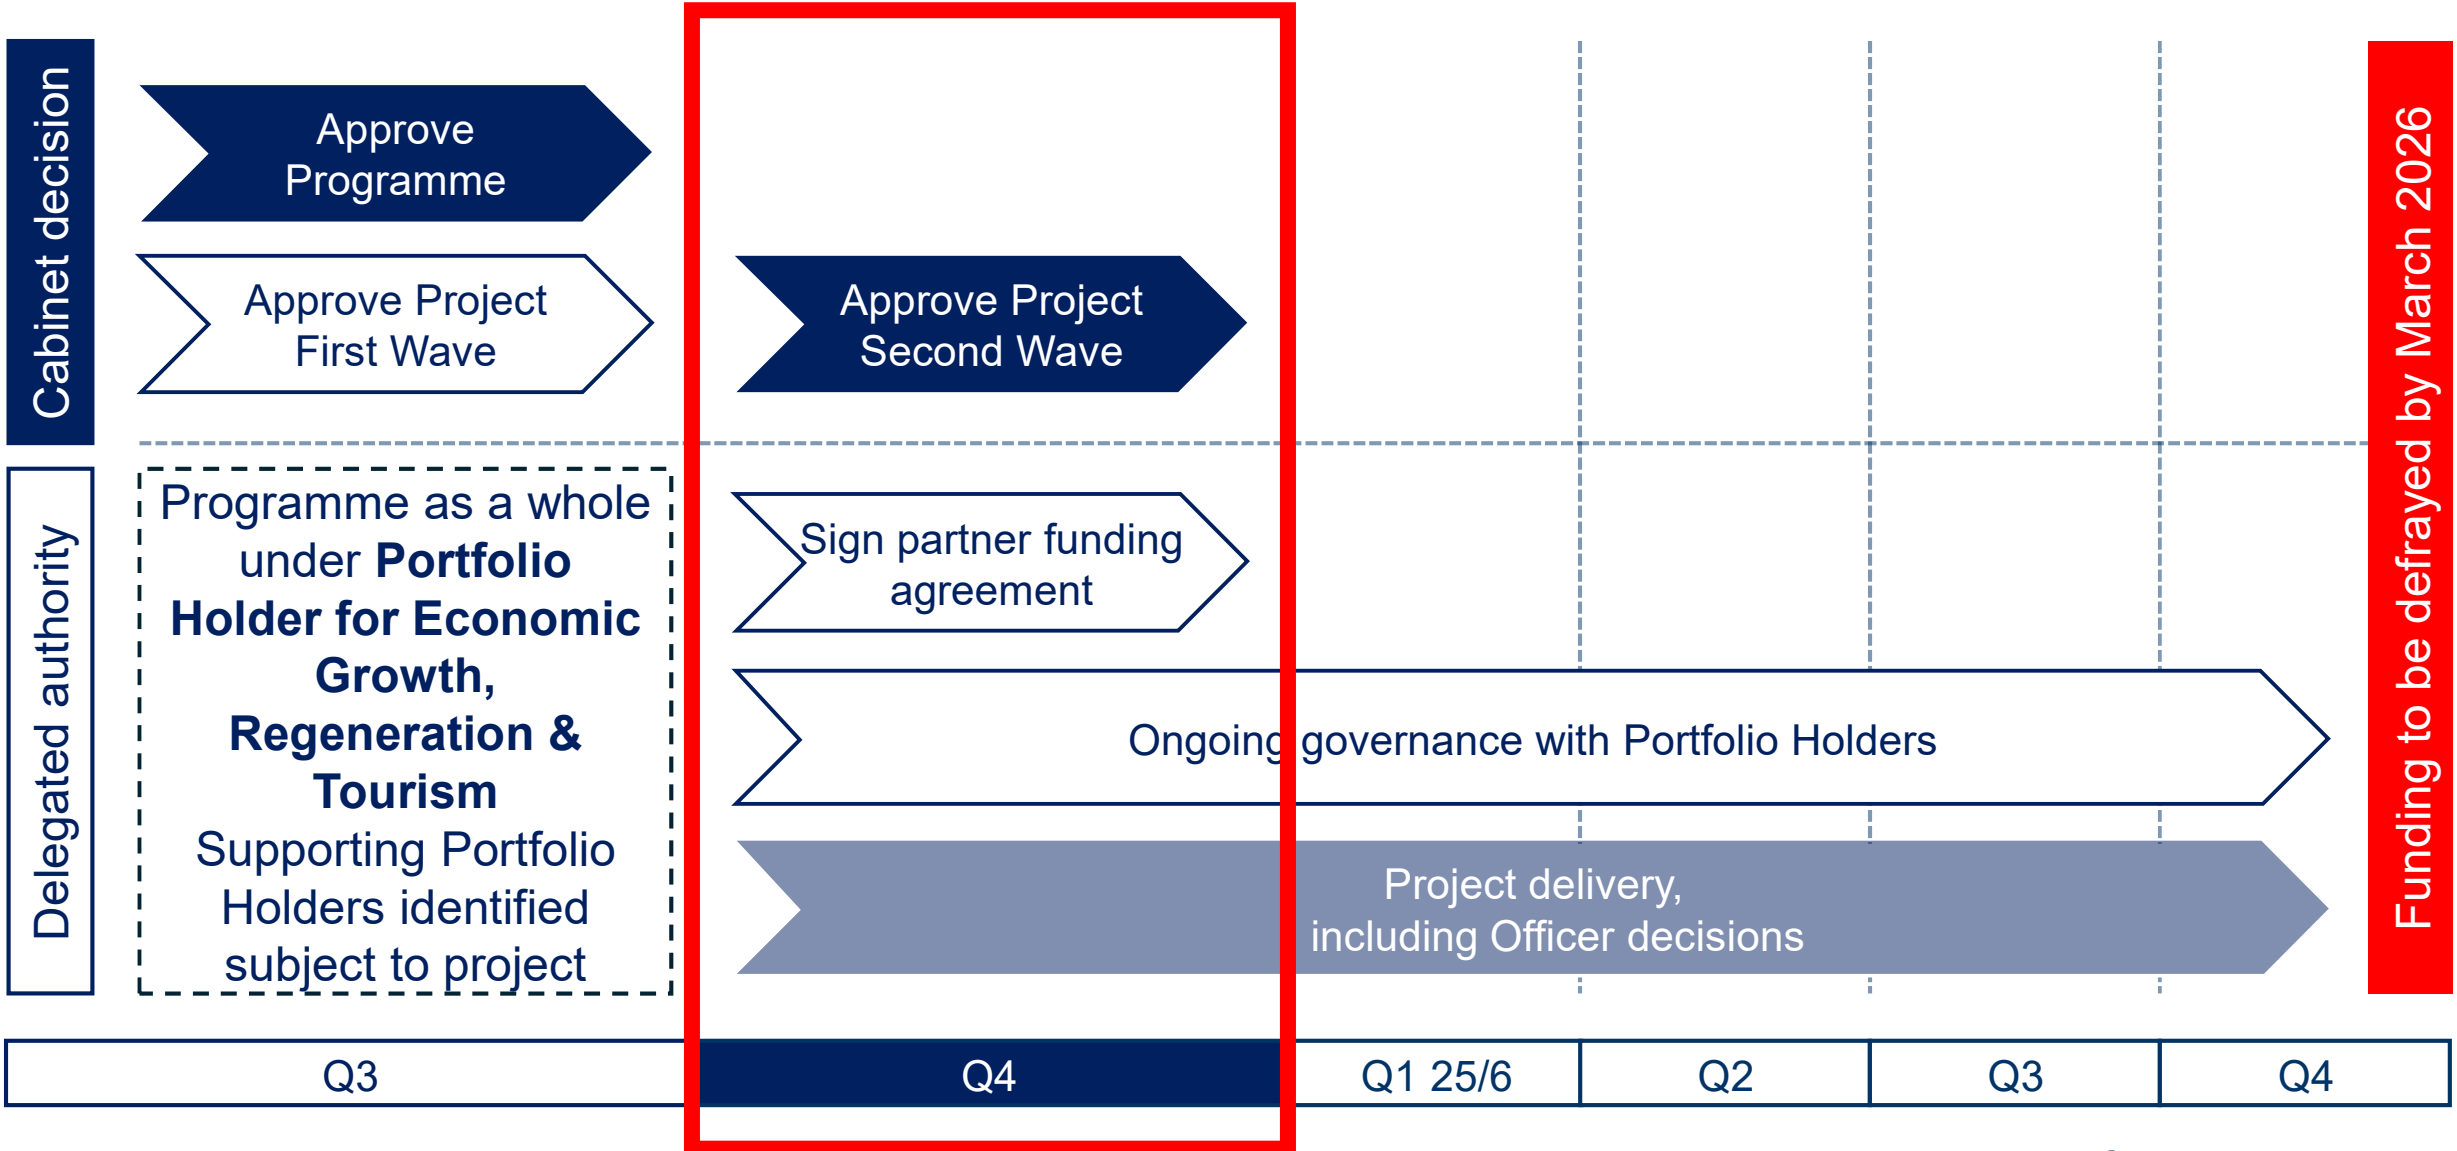

Project status

First wave

Recommendations for next steps




Arts / community micro venue



Shopfront improvements



Community Transport Buses



Healthy Homes Initiative

- Culture
- Town Centre
- Jaywick Sands
- Wellbeing

Second wave

Further clarification on scope



A spatial plan for culture



Martello Tower E



Public open spaces in Jaywick

Third wave

Subject to existing governance



Active Wellbeing Centre



Town Centre Building



Solar panels to Sunspot

Fourth wave


Subject to legal & funding agreement



Improving public realm



Skills Hub fit-out



Bus infrastructure in Clacton & Jaywick



Tudor Fields




Urgent Treatment Centre

The Partnership in 2026

Where will each project be by the funding deadline?



Feasibility of acquiring the **Town Centre Building** will have been established and, subject to outcome, purchase complete



Works to the **Martello Tower E** will have commenced on site, with a building contract in place



Public realm improvements agreed and designed, MoU for funding with ECC and construction progressing



Grant programme for **shopfront improvements** will be awarded and works completed by recipients



Designs developed and works completed on site to transform **public open spaces in Jaywick Sands**



Solar panels to Sunspot installed, running costs reduced and fuel poverty support available




Works complete to new All Wheels Park, repairs completed to centre and brief for **Active Wellbeing Centre** developed



Construction completed at the **Seafront Micro Venue** and tenant preparing to open



A **spatial plan for culture** will be adopted, to drive investment and regeneration in Clacton town centre



Bus infrastructure improvements agreed, MoU with ECC and date of completion in place

ECC

Funding awarded to organisations and **Community Transport Buses** purchased




ECC

MoU agreement in place with ECC and agreed commitment for identified equipment for the **Skills Hub Fit-out**



ECC

Design of **Tudor Fields** walkway/cycle path agreed, funding committed and completion date set



A series of sites improved following acquisition by the **Healthy Homes Initiative**, enforcement continues



NHS

Funds transferred to NHS under MoU and construction of **Urgent Treatment Facility** advanced

Project updates

Current priorities:

- Project documentation
- Project team formation & inception
- Appraisal of project feasibility
- Funding agreements
- Preparation for procurement
- Forward Plan for future governance including where delivered by partners

URN	Project	Wave	PDU	Category	2024		2025												2026		
					Q3	Q4	Q1			Q2			Q3			Q4					
					D	Jan	F	A	M	J	J	A	S	O	N	D	J	F	M		
Ten_02	Community Transport Buses	1	MF	Grant		G	Prepare				Open call			Award			*	Deliver			
Ten_06	Expanding housing work of Jaywick Healthy Homes Initiative	1	AV	Acquisition		G	Prepare				P	Negotiation			G	Purchase			*	Complete	
Ten_08	Jaywick and Clacton shopfront improvements	1	ET	Grant		G	Prepare				Open call			Award			*	Deliver			
Ten_10	Seafront arts/community micro venue	1	ET	Construction		1	once	2			P	P	G	*	3	4	4	5	5	5	5
Ten_09	Jaywick Sands Public Open Space	2	AV	Construction		0	Brief	1	G	P	2	2	◇	P	*	3	4	4	5	5	5
Ten_11	Repurposing Martello Tower E	2	AV	Construction		0	Brief	1		P	2	2	R	◇	P	*	3	4	5	5	5
Ten_14	Cultural masterplanning	2	ET	Strategy		0	Brief	1	G	P	P	*	0	0	0	0	0	0			
Ten_04	Sunspot Centre solar panels	3	MF	Construction			Prep	G		P	P	*	4	5	5						
Ten_12	Active Wellbeing Centre Phase One	3	ET	Construction			Pre	P	1		2	3	3	P	P	P	4	4	5	5	5
Ten_13	[...] Town Centre Building	3	ET	Acquisition			Prepare		G	P	Negotiation			Purchase			*	Complete			
Ten_01	Bus infrastructure in Clacton and Jaywick	4	MF	Construction		G	Brief				Prepare			G	Purcha	Deliver					
Ten_03	Fitting out skills hub at Clacton Hub	4	MF	Purchase		G	Prepare														
Ten_05	Tudor Fields - Jaywick walking route	4	MF	Construction		G	1	1			2	2	2	3	3	3	3	4	4	4	G
Ten_07	Town Centre and Seafront Public Realm	4	MF	Construction		G	1	1			2	3	3	4	4	4	P	P	P	5	5
Ten_15	Urgent Treatment Centre and Primary Care Facility	4	MF	Construction		G	Prepare		*	5											
